

Vertical Platform Lift

Jobsite Preparation
Checklist






146_AMG VPL_JobsitePrepChecklist_032824


1 Upper Landing Gate

Ensure to have solid beams on each side of the gate to properly secure it.

Below is the space required.
For instance, a 36" wide gate requires 44 1/4" (see highlight).

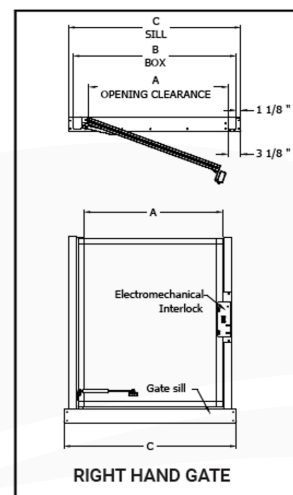

A	B	C
32"	38"	40 1/4"
34"	40"	42 1/4"
36"	42"	44 1/4"
38"	44"	46 1/4"
40"	46"	48 1/4"
42"	48"	50 1/4"

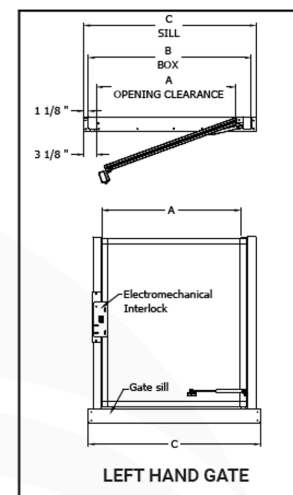

2 Protection Wall

Smooth surface without pinch points from the ground to the first level and must extend 12" on each side of the vertical platform lift.

3 Electrical Outlet

Power supply must be 120 volts / 20 amps.

Needs to be a maximum 10ft within the vertical platform lift location.



IMPORTANT: ALL WORK AND MATERIALS MUST COMPLY WITH ALL LOCAL LAWS AND REGULATIONS.



④ Concrete Slab

7' L x 5' W x 6" D

Minimum of 25 MPA/ 3625 PSI to support 1500 lbs loads.

May need to be winterized depending on location.

⑤ Lifting Height

Confirm height from concrete pad to 1st floor.



LIFTING HEIGHT

IMPORTANT: ALL WORK AND MATERIALS MUST COMPLY WITH ALL LOCAL LAWS AND REGULATIONS.

Jobsite Preparation Checklist

Name: _____

Address: _____

Phone Number: _____

Please ensure there are no obstacles for the technicians

Requirement Checklist:

1. Upper landing gate (required space and structure)
2. Protection wall (remove if installed)
3. Electrical outlet (120V/20A) is installed
4. Concrete slab (7' L x 5' W x 6" D) is installed
5. Lifting height measurement

Please provide the following photos:

- ☐ The concrete slab
- ☐ The protection wall
- ☐ The electrical outlets
- ☐ From the upper landing (side railings)

Notes: _____

I hereby certify that the information provided on this form is true and accurate. Any discrepancies that require the install crew to delay or leave the job site will incur a minimum \$1,500 redeployment fee (Travel expenses will be extra) and must be paid in advance.

Signature: _____

Builder/Homeowner Representative Signature

Date: _____
